



ID	Task Name	Duration	Start	Finish	Predecessors	Oct 16, '05							Oct 23, '05						
						T	W	T	F	S	S	M	T	W	T	F	S	S	M
1	Initial Design Layout	1 day?	Mon 10/17/05	Mon 10/17/05		Initial Design Layout 10/17													
2	Work Break Down structure	1 day?	Mon 10/24/05	Tue 10/25/05		Work Break Down structure 10/25													
3	Flight Controls Budget	3 days?	Mon 10/24/05	Thu 10/27/05	1	Flight Controls Budget 10/27													
4	Management Budget	3 days?	Mon 10/24/05	Thu 10/27/05	1	Management Budget 10/27													
5	Propulsion Budget	3 days?	Mon 10/24/05	Thu 10/27/05	1	Propulsion Budget 10/27													
6	Structure Budget	3 days?	Mon 10/24/05	Thu 10/27/05	1	Structure Budget 10/27													
7	Wing airfoil selection	5 days?	Mon 10/24/05	Mon 10/31/05		Wing airfoil selection 10/31													
8	Predicted weights	5 days?	Mon 10/24/05	Mon 10/31/05	1	Predicted weights 10/31													
9	Design loads	5 days?	Mon 10/24/05	Mon 10/31/05	1	Design loads 10/31													
10	SAE registration	5 days	Mon 10/24/05	Mon 10/31/05		SAE registration 10/31													
11	Budget for funding board	6 days?	Thu 10/27/05	Thu 11/3/05	3,4,5,6	Budget for funding board 11/3													
12	Initial performance studies	10 days?	Mon 10/24/05	Mon 11/7/05	1	Initial performance studies 11/7													
13	Propeller selection	11 days?	Mon 10/24/05	Mon 11/7/05		Propeller selection 11/7													
14	Initial Structural layout/configuration	6 days?	Mon 10/31/05	Mon 11/7/05	1,8,9	Initial Structural layout/c													
15	Start purchasing materials	2 days?	Fri 11/4/05	Mon 11/7/05	11														
16	Wing planform	11 days?	Mon 10/31/05	Mon 11/14/05	1,9	Wi													
17	Landing gear study	5 days?	Tue 11/8/05	Mon 11/14/05	14														
18	Belt/Gear configuration	5 days?	Tue 11/8/05	Mon 11/14/05	13														
19	Intial Control system configuration	5 days?	Tue 11/15/05	Mon 11/21/05	1,16,17														
20	CFD Model	5 days?	Tue 11/15/05	Mon 11/21/05	1,7,16														
21	Plan for building	15 days?	Tue 11/8/05	Mon 11/28/05	15														
22	Start building plane!!!!	5 days?	Tue 11/29/05	Sat 12/3/05	15,21														
23	Initial Report Write Up	5 days?	Mon 12/5/05	Fri 12/9/05															
24	Registration	32 days?	Mon 10/31/05	Mon 12/12/05	10														
25	Detailed design	56 days?	Tue 10/25/05	Tue 1/10/06	1	Detailed design 1/10													
26	Detailed Structural layout/configuratio	47 days?	Tue 11/22/05	Tue 1/24/06	14,16,17,19														
27	Detailed Control system configuration	37 days?	Tue 11/22/05	Tue 1/10/06	19														
28	Detailed Propulsion configuration	37 days?	Tue 11/22/05	Tue 1/10/06	13,18														
29	Detailed performance studies	20 days?	Wed 1/25/06	Tue 2/21/06	12,26,27,28														
30	Report Deadline (postmarked)	65 days?	Mon 12/12/05	Fri 3/10/06	23														

Project: WBS Date: Mon 11/7/05	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	

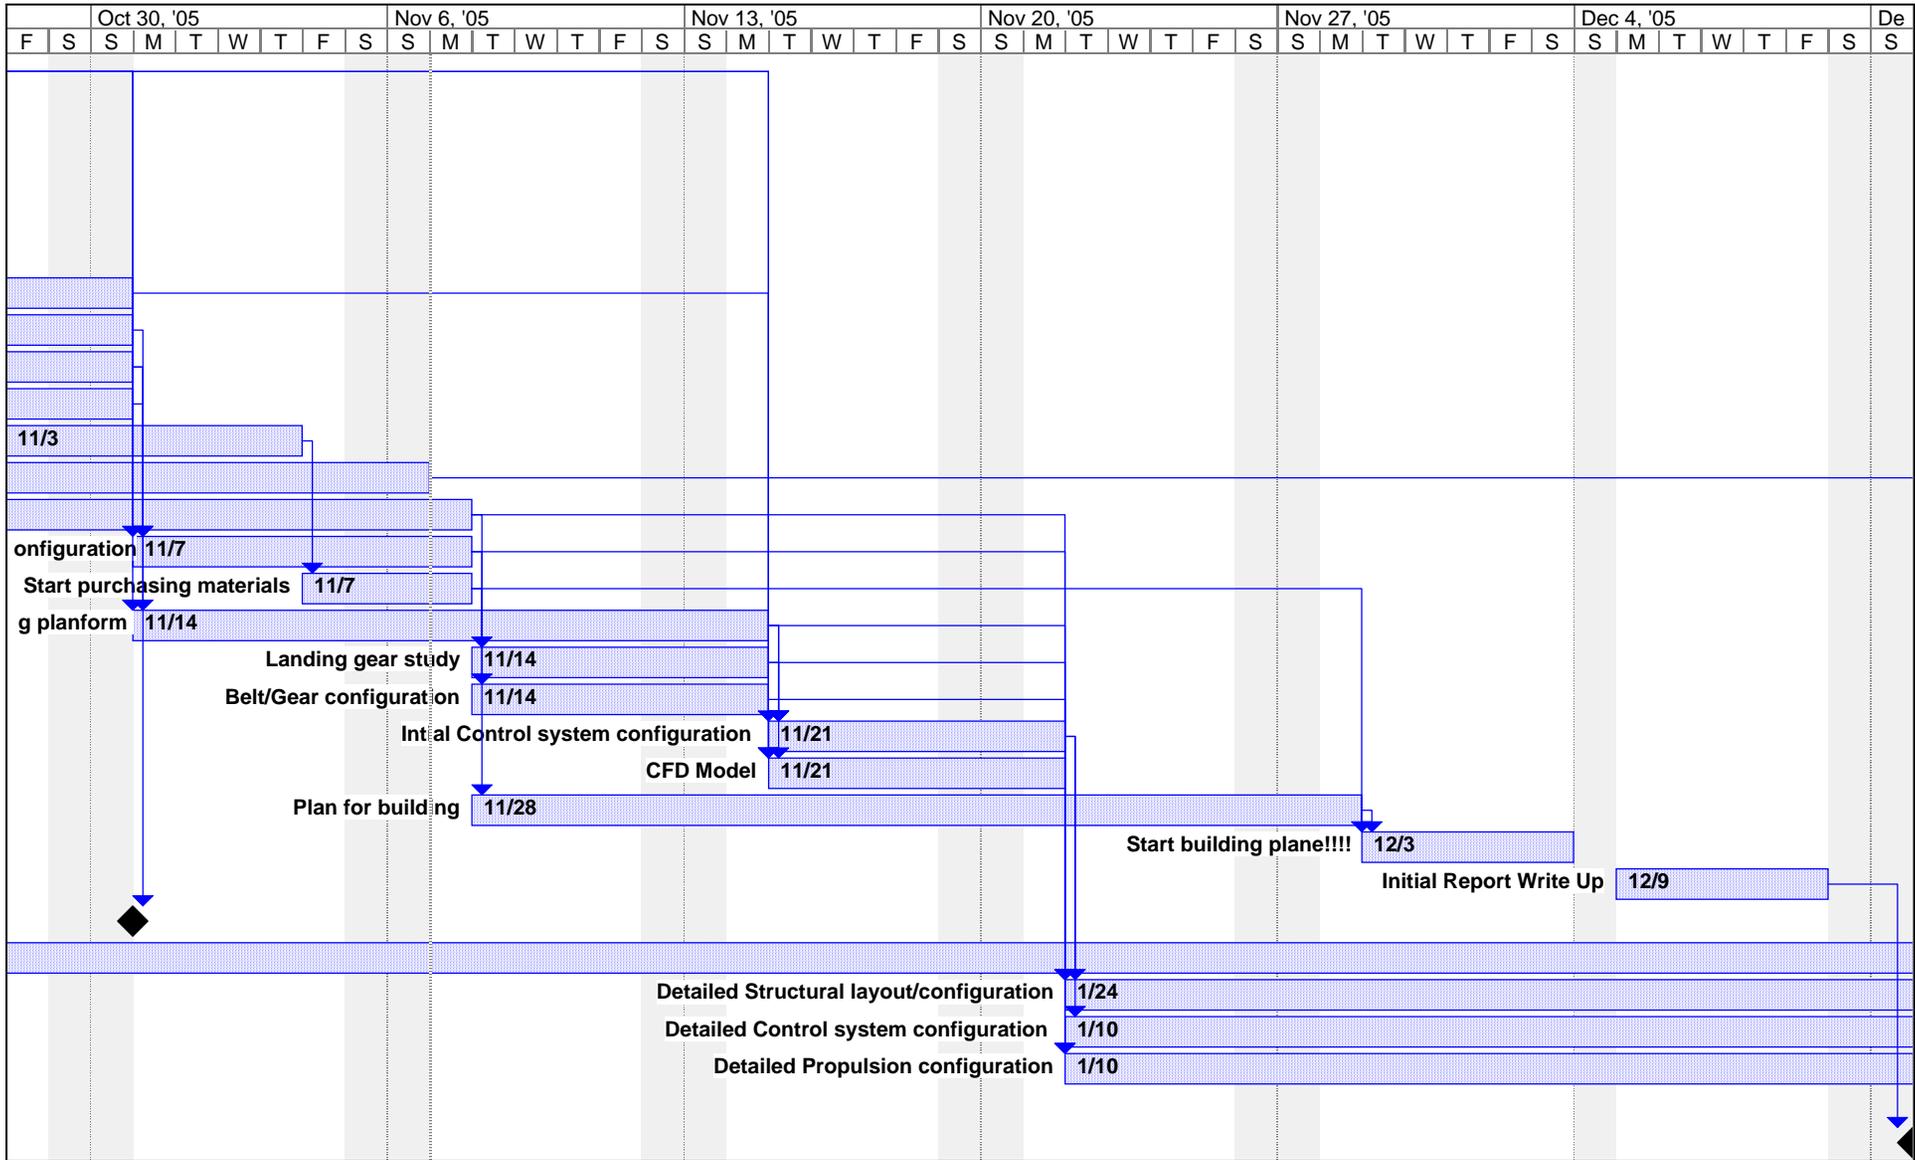


Project: WBS Date: Mon 11/7/05	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	

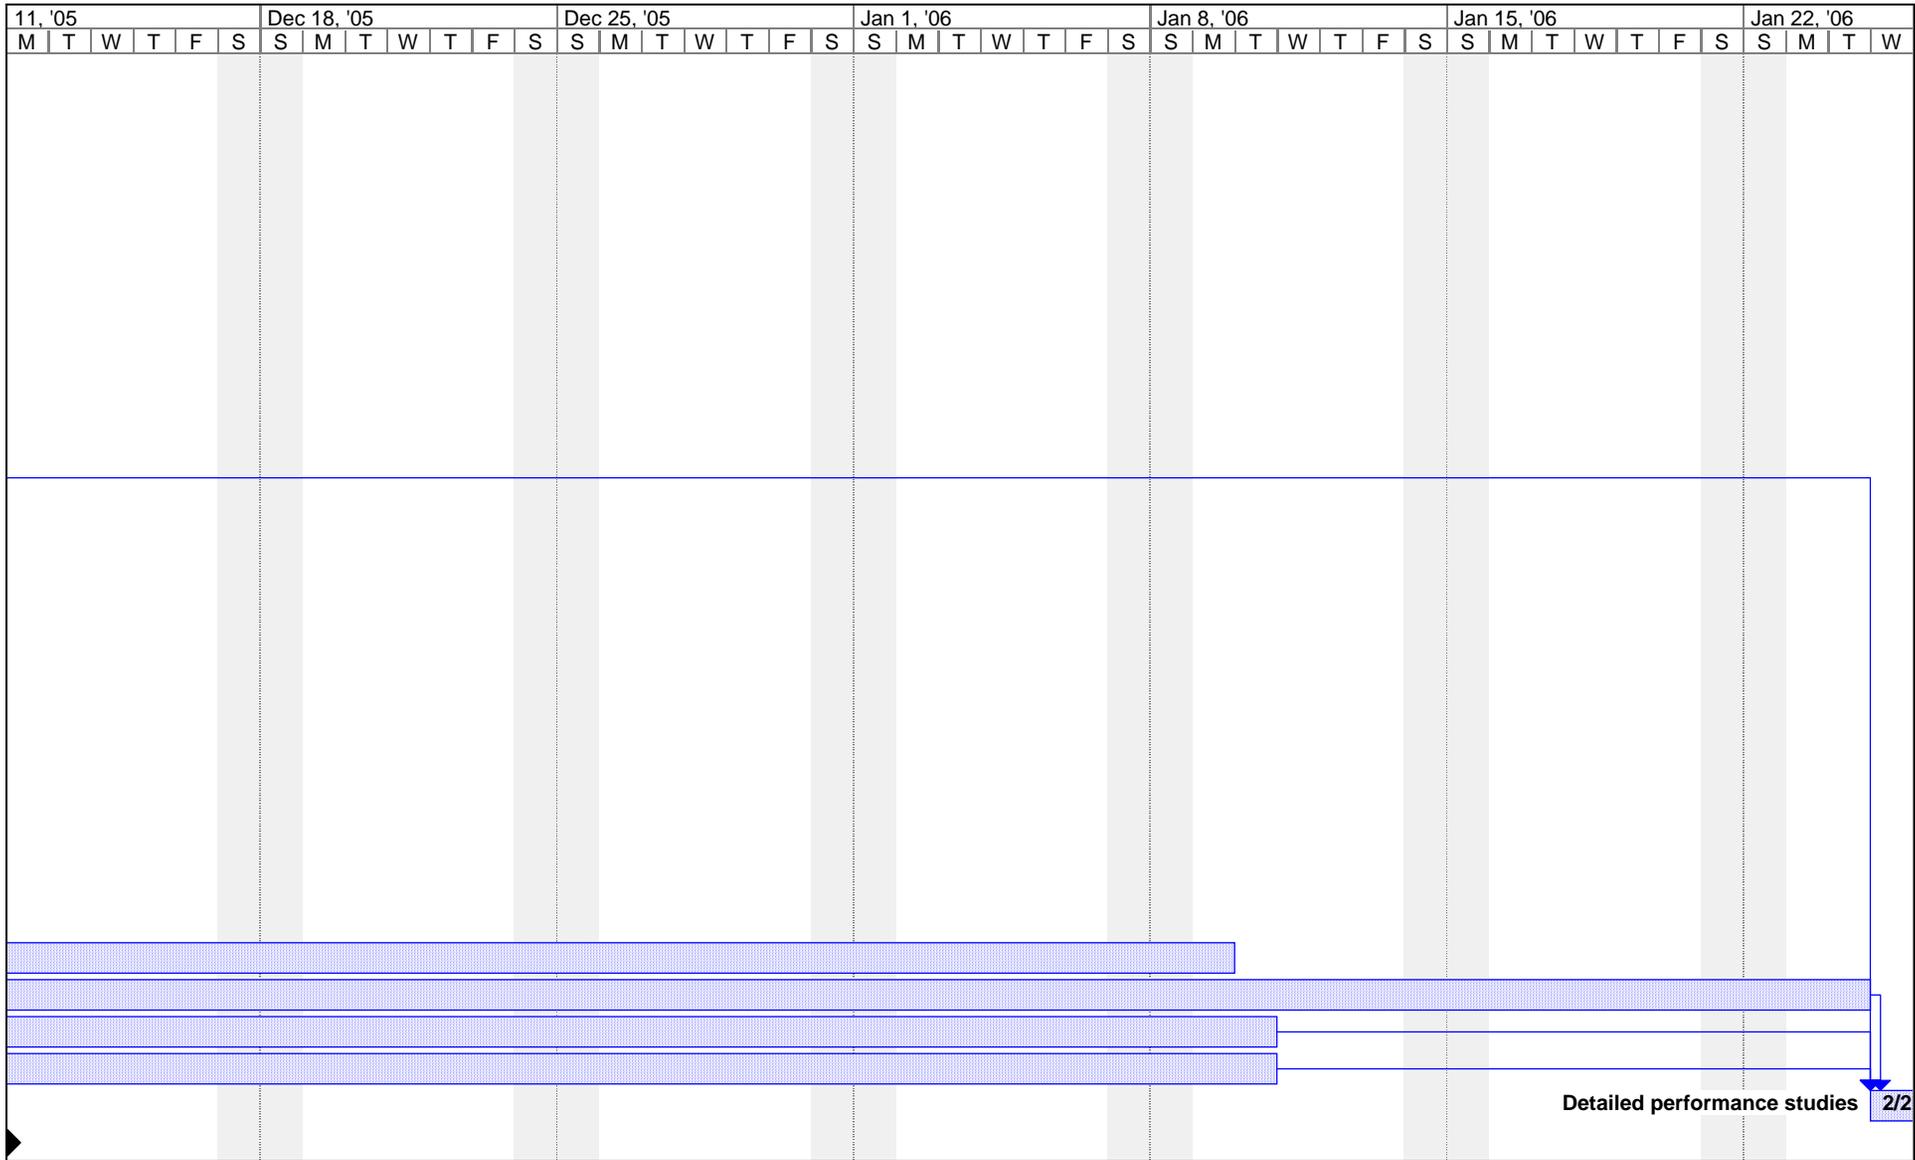


Project: WBS  
Date: Mon 11/7/05

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone		Project Summary	
Milestone		Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	

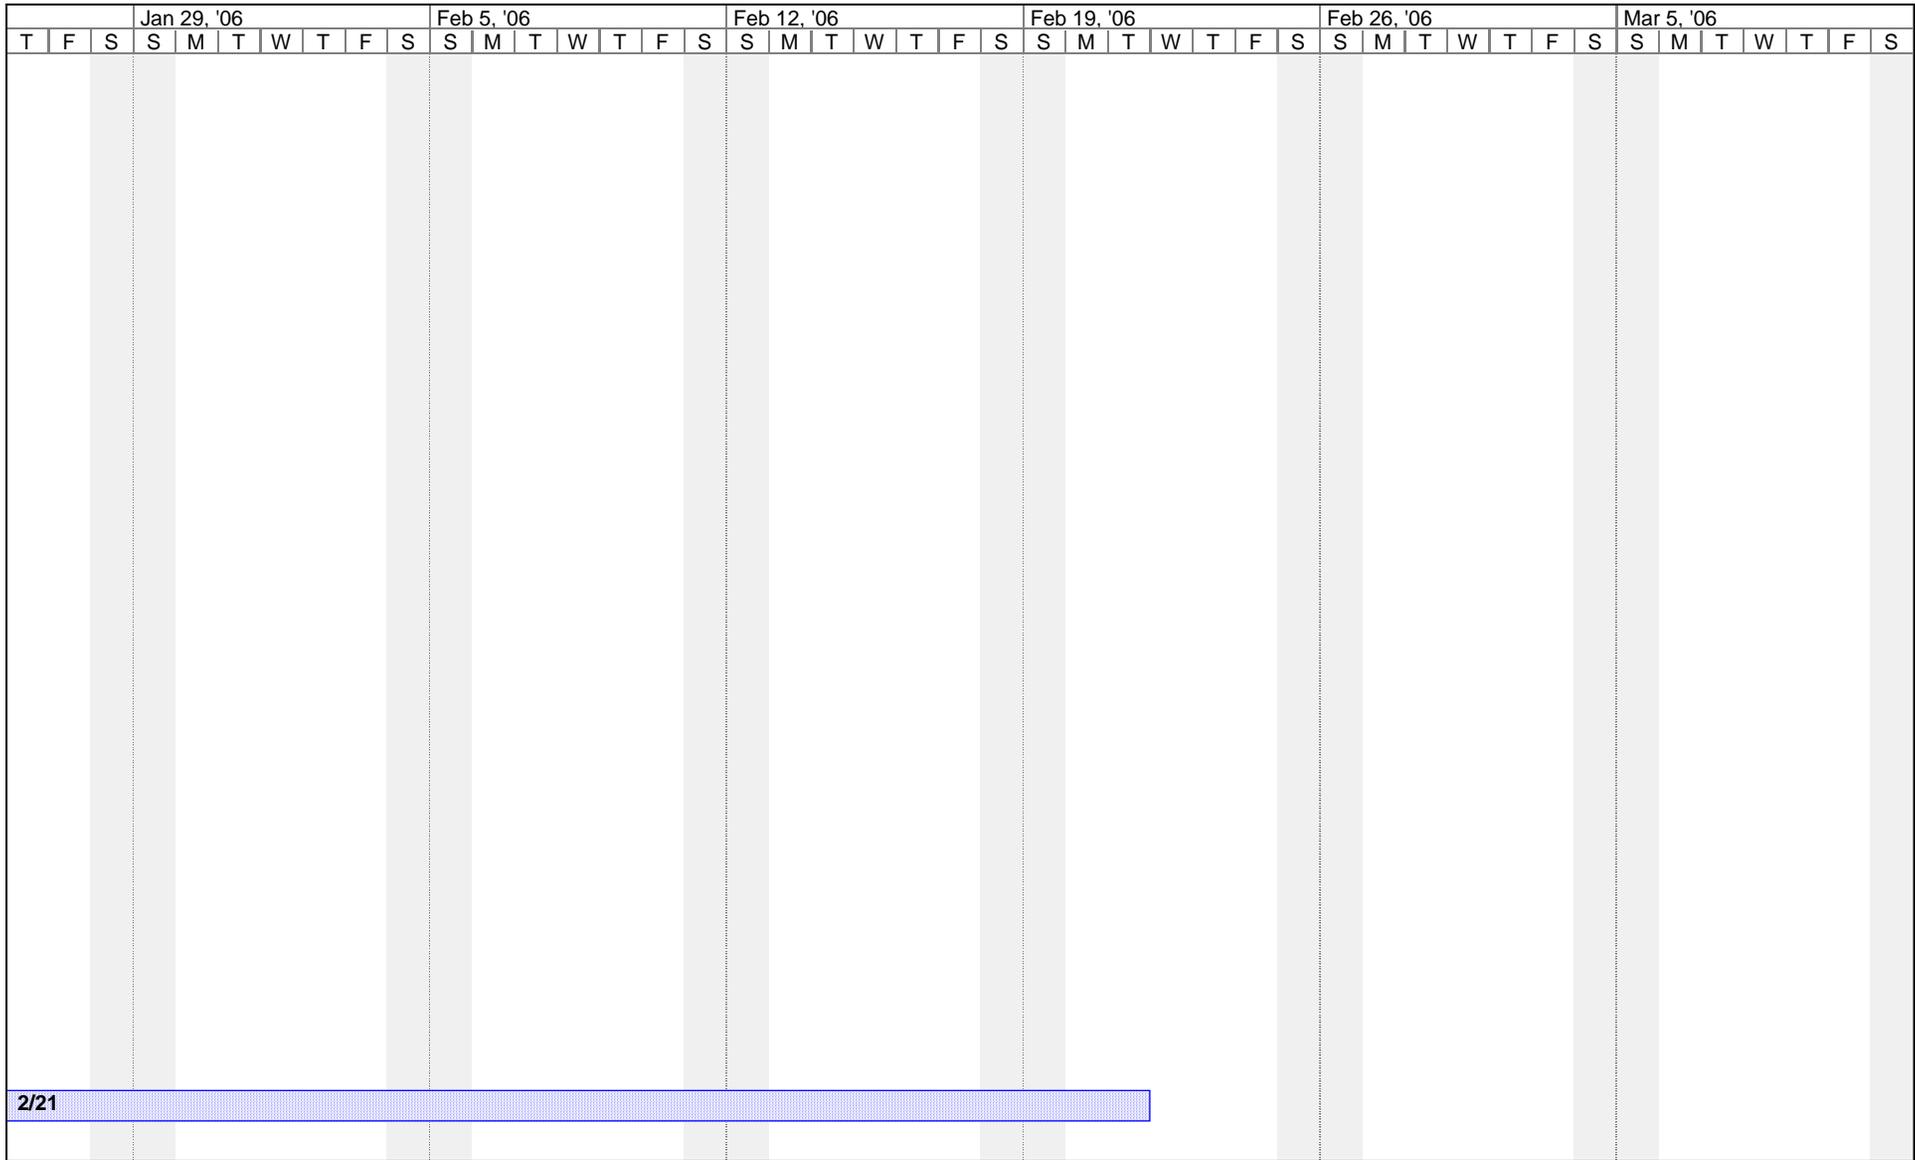

Project: WBS  
Date: Mon 11/7/05

Task		Rolled Up Task		External Tasks	
Progress		Rolled Up Milestone		Project Summary	
Milestone		Rolled Up Progress		Group By Summary	
Summary		Split		Deadline	
